

Black Country LEP Growth Deal Dashboard as at 1st May 2019 v1.0


Summary 2 of 2 – FUTURE YEARS

SPEND PROFILE

Growth Deal 1, 2 & 3 Funding Profile

	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Total
LGF Competitive	£23.70	£33.25	£11.94	£4.44	£7.13	£0.03	£80.49
LGF DfT Retained (M6 J10)	£0.65	£0.35	£0.12				£1.12
LGF DfT Competitive (M6 J10)					£13.93	£14.60	£28.53
LGF Expansion		£3.90	£3.60	£3.60	£6.40	£6.40	£23.90
GD 3			£12.82	£10.39	£5.32	£26.52	£55.05
Total LGF Commitment	£24.35	£37.50	£28.48	£18.43	£32.78	£47.55	£189.09
LTB pre-allocated	£5.60	£8.80	£2.90	£1.10	£0.20		£18.60
Existing DfT transport major*	£3.60						£3.60
Total Other	£9.20	£8.80	£2.90	£1.10	£0.20	£0.00	£22.20
Total Growth Deal	£33.55	£46.30	£31.38	£19.53	£32.98	£47.55	£211.29

Programme Funding vs Spend (Cumulative £m)

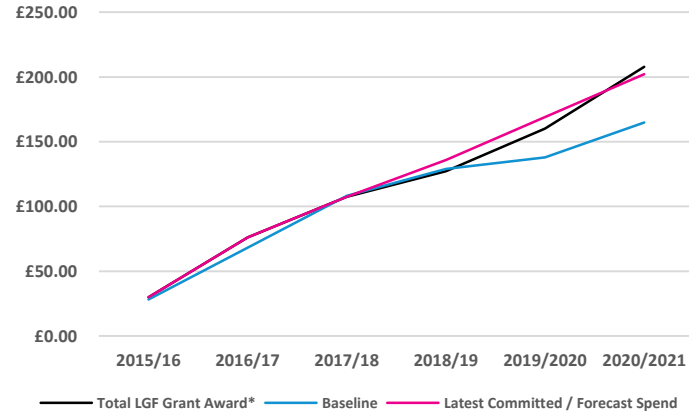

Competitive LGF Funding (£m)

	15/16	16/17	17/18	18/19	19/20	20/21	Total
Total LGF Grant Award*	£29.95	£46.30	£31.38	£19.53	£32.98	£47.55	£207.69
Baseline	£28.33	£39.97	£39.89	£20.86	£8.81	£26.88	£164.73
Latest Committed / Forecast Spend	£29.95	£46.30	£31.38	£21.07	£40.35	£40.70	£209.76
Over/Under-utilisation of Grant Funding	£0.00	£0.00	£0.00	£1.54	£7.37	£-6.85	£2.08

*Inc. GD 1, 2 & 3 Competitive, LTB Pre-Committed Funds & DfT for M6 J10

➤ PMO and Accountable Body are working closely together to finalise the final two years of the Programme.


*tail funding for Darlaston

OUTPUTS – TO BE REALISED POST PROJECT DELIVERY

Includes Direct outputs only, subject to validation by Walsall Accountable Body

Outputs	Forecast by Year						Forecast to 2021	Total Forecast	Actual to Date	
	2015-2017	2017/18	2018/19	2019/20	2020/21	2021+				
Jobs	Jobs Created	510	533	620	615	1,555	43	3,833	3,876	507
	Jobs Safeguarded	121	9	537	164	150	0	981	981	296
Houses	Homes Started	557	464	702	131	98	0	1,952	1,952	740
	Homes Completed	341	296	108	149	162	0	1,056	1,056	693
Business Assists	# new enterprises receiving non financial support	0	5	4	16	6	0	31	31	6
	# of enterprises receiving non financial support	134	157	808	450	473	120	2,022	2,142	228
	# of enterprises receiving grant support	16	15	7	0	0	0	38	38	39
	# of enterprises receiving financial support other than Grant	53	0	0	25	28	0	106	106	0
	# of potential entrepreneurs assisted to be enterprise ready	73	59	51	55	62	0	300	300	87
Total Business Assists	276	236	870	546	569	115	2,497	2,612	354	
Learner Assists	Learner Assists	2,303	2,353	4,076	3,480	3,616	524	15,828	16,352	5,355
	Apprenticeships Started	622	1,100	1,209	1,337	1,176	467	5,444	5,911	3,333
	Apprenticeships Completed	204	259	638	800	895	224	2,796	3,020	730
Land and Property	New build / refurbished training/ learning space (sqm)	3,903	4,327	802	0	0	5,008	9,032	14,040	8,030
	Commercial floorspace constructed / Refurbished Gross (sqm)	20,042	30,939	10,682	17,355	22,107	0	101,125	101,125	51,608
	Area of site reclaimed, (re)developed or assembled (ha)	27	8	12	7	22	0	76	76	11
Visitor Economy	Visitor Numbers	63,925	68,195	65,217	100,250	170,268	180,000	467,855	647,855	63,984
Infrastructure	Total Length of Resurfaced Roads (Km)	13	1	5	0	0	0	18.45	18.45	13.58
	Total Length of Newly Built Roads (Km)	6	0	2	0	0	0	7.82	7.82	5.99
	Total Length of New Cycleway (km)	37	7	9	0	0	0	52.66	52.66	45.58

Achievement against Direct Output Forecast 2015/16 - 2020/21 +

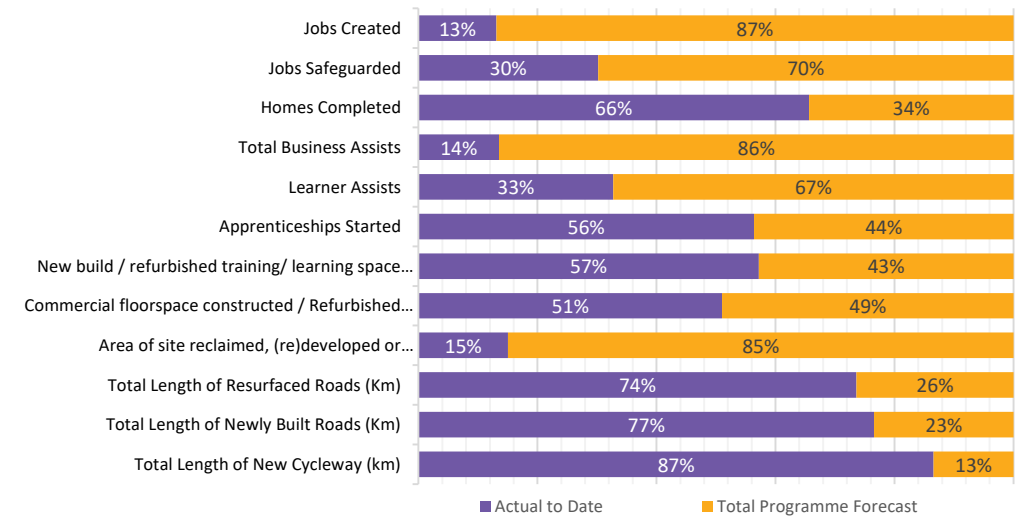

GROWTH DEAL 1, 2 & 3 FUNDING COMMITMENT FULL PROGRAMME 2015/16 – 2020/21

PROJECT NAME	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Total LGF
	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	
Garden City							
Completed Projects		£0.06					£0.06
Bilston Urban Village	£2.75	£2.09					£4.84
Goscote Lane Corridor	£1.70	£2.81	£4.31				£8.82
Woods Lane	£0.55	£2.53	£0.98	£0.35	£0.36		£4.77
Walsall Waterfront	£0.03	£0.10	£0.01				£0.15
Dudley Brownfield Land - Ph 1		£0.99	£0.72	£0.73			£2.43
Holloway Street, Gornal (SI)			£0.04				£0.04
Reedswood (former) Golf Course (SI)			£0.01				£0.01
Sandwell Residential Programme SI				£0.06			£0.06
Woods Lane Phase 2				£1.70			£1.70
HVM City							
Completed Projects	£0.30	£1.74	£0.02				£2.06
Growing Priority Sectors	£1.49	£1.34	£1.67	£4.13			£8.63
Airfield Drive			£0.37				£0.37
Very Light Rail SEED Funding		£0.64	£1.04				£1.68
Wharf Approach, Aldridge (SI)				£0.03			£0.03
Shidas Lagoon (SI)			£0.00	£0.12			£0.12
Former Willenhall ST Works (SI)			£0.04	£0.10			£0.14
Bilston Urban Village East SI				£0.07			£0.07
Phoenix 10 Phase 1				£1.94			£1.94
The Leather Industry Expansion				£0.45			£0.45
Economic Capital							
Completed Projects	£0.17	£0.32					£0.49
Wolverhampton Civic Hall	£1.88	£2.30	£1.23				£5.41
Chances Glassworks Site Assembly				£0.36			£0.36
Refurbishment of 203/204 Wolverhampton Street, Dudley			£0.15				£0.15
Challenge Block (SI)			£0.02	£0.02			£0.04
Black Country Living Museum (SI)		£0.02	£0.00				£0.02
Church Square Apartments				£0.12			£0.12
Hatherton Street Phase 2					£0.80		£0.80
19 Wolverhampton				£0.95	£2.96	£0.08	£4.00
Black Country Living Museum - Forging Ahead					£2.63	£6.37	£9.00
Very Light Rail Development Funding				£0.31			£0.31
Skills Capital							
Completed Projects	£5.92	£11.05	£1.40	£0.48			£18.86
Elite Centre for Manufacturing Skills		£1.75	£5.97	£0.82			£8.55
City Learning Quarter (SI)				£0.12			£0.12
University College Dudley (UCD) SI				£0.06			£0.06
Halesowen College - Business & Construction Management Centre				£0.69	£3.02	£2.22	£5.93
School of Architecture and Built Environment					£3.52		£3.52
Springfield Phase 1 Infrastructure and Remediation					£4.42		£4.42
National Brownfield Institute SEED Funding					£0.50		£0.50
Local Transport Solutions							
Completed Projects	£2.43	£3.86					£6.29
Accessing Growth Programme	£1.99	£5.69	£1.77	£2.38	£2.97		£14.80
Wolverhampton Interchange Commercial Gateway Phase 2	£4.50		£3.50				£8.00
M6 Junction 10	£0.65	£0.35	£0.12		£13.94	£14.59	£29.65
Major Transport Scheme						£7.62	£7.62
Managing Short Trips Tranche 2			£2.02	£2.23			£4.25
City North Gateway Phase 1			£2.32	£1.03			£3.35
Birchley Island Main Scheme				£0.33	£1.21	£8.70	£10.24
I54 Western Extension Access Package					£2.50	£0.50	£3.00
PROGRAMME MANAGEMENT & DEVELOPMENT							
JC Programme Expenditure	£0.13	£0.20	£0.18	£0.23	£0.18	£0.18	£1.08
LEP Programme Management	£0.26	£0.30	£0.20	£0.27	£0.18	£0.18	£1.40
Black Country Transport Expenditure	£0.21	£0.21	£0.25	£0.10	£0.10	£0.10	£0.98
Programme Technical Advisors		£0.04	£0.04	£0.16	£0.17	£0.16	£0.56
LA Programme Work and Development	£0.42	£0.76	£0.76				£1.93
Total Committed / Forecast Spend LGF	£25.38	£39.13	£29.15	£20.34	£39.45	£40.70	£194.16
LTB PROJECTS							
Local Transport Solutions - LTB							
M6 Junction 10 (LTB)	£0.10		£0.20				£0.30
Wolverhampton Interchange Commercial Gateway Phase 2 (LTB)	£4.37	£4.63					£9.00
Birchley Island M5 J2	£0.10						£0.10
A4101 Pensnett Strategic Access Improvement Scheme		£2.35	£1.45				£3.80
LTB Development Funding Total		£0.19	£0.58	£0.73	£0.07		£1.57
LTB Unallocated Funds (Aldridge Station)					£0.83		£0.83
Total Committed / Forecast Spend LTB	£4.57	£7.17	£2.23	£0.73	£0.90		£15.60
Grand Total	£29.95	£46.30	£31.38	£21.07	£40.35	£40.70	£209.76

Leverage	Total Project Investment
£0.00	£0.06
£81.25	£86.09
£78.59	£87.41
£43.79	£48.56
£0.31	£0.45
£27.61	£30.04
£0.00	£0.05
£0.00	£0.01
£0.02	£0.08
£13.20	£14.90
£14.87	£16.93
£18.00	£26.63
£4.71	£5.08
£0.00	£1.68
£0.00	£0.03
£0.00	£0.12
£0.00	£0.14
£0.04	£0.11
£0.00	£1.94
£1.05	£1.50
£5.43	£10.84
£0.06	£0.42
£0.46	£0.61
£0.00	£0.04
£0.00	£0.02
£0.31	£0.43
£2.03	£2.83
£12.90	£16.89
£14.69	£23.69
£0.00	£0.31
£6.35	£10.66
£4.15	£12.70
£0.03	£0.09
£2.54	£8.47
£37.35	£40.87
£2.08	£6.50
£0.00	£0.50
£0.21	£6.51
£1.88	£16.68
£105.20	£113.20
£34.55	£64.20
£34.55	£42.17
£0.16	£4.41
£0.75	£4.10
£9.49	£19.74
£38.70	£41.70
£0.00	£1.08
£0.00	£1.40
£0.00	£0.98
£0.00	£0.56
£0.00	£1.93
£597.31	£776.31
As Above	£0.30
As Above	£9.00
£0.00	£0.10
£2.50	£6.30
£0.00	£1.57
TBC	£0.83
£2.50	£18.10
£599.81	£794.41

	2015/16	2016/17	2017/18	2018/19	2019/2020	2020/2021	Total
Total LGF Grant Award (LGF/LTB/M6 J10)	£29.95	£46.30	£31.38	£19.53	£32.98	£47.55	£207.70
Utilisation of Grant Funding	£29.95	£46.30	£31.38	£21.07	£40.35	£40.70	£209.76
Variance	£0.00	£0.00	£0.00	£1.54	£7.37	£-6.85	£2.07

GROWTH DEAL SUMMARY OF PROJECTS IN OUTPUT MONITORING – TO DATE

PROJECT NAME	Borough	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Total LGF
		TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	
Advanced Science, Engineering & Technology Centre (Halesowen College)	Dudley	£1,059,000	£0	£0	£0	£0	£0	£1,059,000
Dudley Advance Construction Centre	Dudley	£2,028,108	£5,851,892	£0	£0	£0	£0	£7,880,000
Fab Kit - Fab Lab (Sandwell College)	Sandwell	£36,300	£0	£0	£0	£0	£0	£36,300
Fab Kit - In-Comm	Walsall	£141,000	£0	£0	£0	£0	£0	£141,000
Fab Kit - PTP	Walsall	£98,787	£0	£0	£0	£0	£0	£98,787
Science, Technology & Prototyping Centre	W'hampton	£1,296,594	£3,583,406	£0	£0	£0	£0	£4,880,000
Ruskin Mill Glasshouse - Phase 3	Dudley	£160,026	£0	£0	£0	£0	£0	£160,026
Dudley Town Centre - Sites & Buildings Improvements	Dudley	£169,558	£285,442	£0	£0	£0	£0	£455,000
Walsall College - Improving Engineering Capacity	Walsall	£207,128	£0	£0	£0	£0	£0	£207,128
University of Wolverhampton Apprenticeship Hub	W'hampton	£150,000	£50,000	£0	£0	£0	£0	£200,000
Walsall College - Microsoft IT Academy	Walsall	£147,768	£0	£0	£0	£0	£0	£147,768
PTP IT Academy	Walsall	£40,000	£0	£0	£0	£0	£0	£40,000
Airfield Drive	Walsall	£0	£0	£370,993	£0	£0	£0	£370,993
Halesowen College - Access Centre for HE	Dudley	£0	£699,795	£0	£0	£0	£0	£699,795
Dudley College - Advanced Engineering Equipment	Dudley	£0	£104,400	£0	£0	£0	£0	£104,400
Walsall College – Additional Engineering Equipment	Walsall	£0	£149,250	£0	£0	£0	£0	£149,250
Dudley College - Construction Apprenticeship Training Centre	Dudley	£0	£507,247	£92,753	£0	£0	£0	£600,000
Advanced Manufacturing Training Centre	Walsall	£0	£0	£722,999	£0	£0	£0	£722,999
Refurbishment of 203/204 Wolverhampton Street, Dudley	Dudley	£0	£0	£145,947	£0	£0	£0	£145,947
Walsall Waterfront	Walsall	£31,638	£100,771	£14,965	£0	£0	£0	£147,374

*Projects in output monitoring have spent all Growth Deal Grant funding awarded, initial physical delivery is completed and contracted outputs are to be delivered over an agreed period of time. (monitored until March 2021)

GROWTH DEAL – COMPLETED TRANSPORT DEVELOPMENT FUNDING SUMMARY – TO DATE

PROJECT NAME	Borough	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Total LGF
		TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	
Dudley Bus Station	Dudley	£0	£157,677	£42,323	£0	£0	£0	£200,000
Bloxwich Mitigation Package	Walsall	£0	£0	£100,000	£0	£0	£0	£100,000
Birchley Island M5 J2	Sandwell	£100,000	£0	£0	£0	£0	£0	£100,000
West Coast Mainline HS2 Study	Walsall / Sandwell	£0	£0	£40,000	£40,000	£0	£0	£80,000

*It is expected that a Capital Scheme will follow on from Transport Development funding.

GROWTH DEAL - CLOSED PROJECT SUMMARY – TO DATE

PROJECT NAME	Borough	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Total LGF
		TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	TOTAL	
Accessing Growth - Bilston Urban Village Access Package	W'hampton	£726,627	£2,168,661	£0	£0	£0	£0	£2,895,288
Accessing Growth - Junction & Highway Improvements (Canal Side)	Sandwell	£630,000	£0	£0	£0	£0	£0	£630,000
Managing Short Trips	BC Wide	£2,430,009	£3,860,836	£0	£0	£0	£0	£6,290,845
Accessing Growth - WCC Coach Station	W'hampton	£387,673	£90,000	£0	£0	£0	£0	£477,673
Accessing Growth - M6 J10 Resilience Package	Walsall	£94,519	£1,235,176	£0	£0	£0	£0	£1,329,695
Accessing Growth - Wednesbury to Brierley Hill Metro	Dudley	£0	£400,000	£0	£0	£0	£0	£400,000
Accessing Growth - Compton Park Improved Connectivity	W'hampton	£149,352	£0	£0	£0	£0	£0	£149,352
Accessing Growth - Springfield Campus Interchange Connectivity	W'hampton	£0	£600,000	£0	£0	£0	£0	£600,000
Accessing Growth - A459 Dudley Road/Coombs Road Halesowen	Dudley	£0	£259,291	£280,709	£0	£0	£0	£540,000
Accessing Growth - Pinfold Bridge, Wednesfield Road, Wolverhampton	W'hampton	£0	£674,568	£0	£0	£0	£0	£674,568
Accessing Growth - City East Gateway - A454 Willenhall Road Corridor	W'hampton	£0	£158,800	£26,517	£0	£0	£0	£185,317
Accessing Growth - City North Gateway - A449 Stafford Road Corridor	W'hampton	£0	£101,011	£13,336	£0	£0	£0	£114,347
Accessing Growth - B4176 Himley Rd Junction Improvements	Dudley	£0	£0	£78,500	£0	£0	£0	£78,500
Accessing Growth - M6 J10 (Major)	Walsall	£0	£0	£218,834	£0	£0	£0	£218,834
Elite Centre for Manufacturing Skills - Feasibility Study	W'hampton	£170,000	£0	£0	£0	£0	£0	£170,000
Accessing Growth - North Smethwick Canalside Access	Sandwell	£630,000	£0	£0	£0	£0	£0	£630,000
CWC Relocation - Campus Realignment - Feasibility Study	W'hampton	£310,000	£0	£0	£0	£0	£0	£310,000
Music Institute - Feasibility Study	Dudley	£80,000	£70,000	£0	£0	£0	£0	£150,000
Very Light Rail Innovation Centre - Feasibility Study	Dudley	£150,000	£150,000	£0	£0	£0	£0	£300,000
Birchley Island Development Funding	Sandwell	£100,000	£0	£0	£0	£0	£0	£100,000
Very Light Rail Innovation Centre - SEED Funding	Dudley	£0	£637,814	£198,914	£0	£0	£0	£836,728
A4101 Pensnett High Street	Dudley	£0	£2,348,432	£1,451,569	£0	£0	£0	£3,800,001

*Closed projects have spent all Growth Deal Grant Funding, practical completion and contracted Outputs delivered.

GROWTH DEAL – COMPLETED SITE INVESTIGATION SUMMARY – TO DATE

PROJECT NAME	Borough	2015/16	2016/17	2017/18	2018/19	2019/20	2020/21	Commentary
Bourne St, Coseley (SI)	Dudley	£0	£63,565	£0	£0	£0	£0	Main scheme is awaiting planning permission
Pope's Lane (SI)	Sandwell	£54,301	£0	£0	£0	£0	£0	Capital Scheme completed 17/18
Pensnett (SI)	Dudley	£41,165	£0	£0	£0	£0	£0	Capital Scheme completed 17/18
Reedwood (former) Golf Course (SI)	Walsall	£0	£0	£9,330	£0	£0	£0	SI completed, awaiting a capital scheme to come forward
Holloway Street, Gornal (SI)	Dudley	£0	£0	£43,100	£0	£0	£0	SI completed, awaiting a capital scheme to come forward
Parkrose Industrial Estate (SI)	Sandwell	£53,994	£19,170	£0	£0	£0	£0	Capital Scheme underway without LEP Funding
Moxley Business Park (SI)	Walsall	£0	£88,600	£0	£0	£0	£0	Main scheme progressing through LPIF
Bull Street (SI)	Sandwell	£0	£34,761	£0	£0	£0	£0	SI completed, awaiting a capital scheme to come forward
Black Country Living Museum (SI)	Dudley	£0	£20,148	£3,821	£0	£0	£0	Main scheme progressing through LPIF
Music Institute (SI)	Dudley	£0	£32,579	£0	£0	£0	£0	Main scheme progressing through LPIF

*It is expected that a Capital Scheme will follow on from Site Investigation funding. Sufficient underwriting or clawback is agreed at time of Grant Award for Site Investigations
